



WATER-RIGHT DOCKET

Grand Teton National Park

Docket No: 36

LAKE PIPE LINE DITCH. BEAVER DICK LAKE

Preliminary Docket Information

10-29-1941: water right record for lake pipe line ditch: identification no. grte l1344116af36; permit 19705

WATER RIGHT RECORD

Docket Number 36

Alien WR Number

Water Use Map NP-GT 2174

Sheet Number 5

IDENTIFICATION NO: GRTE L 1 3 4 4 1 1 6 A F 3 6

DITCH/WATER SYSTEM: LAKE PIPE LINE DITCH

SOURCE OF SUPPLY: Beaver Dick Lake, Tributary of Jenny Lake, Tributary of
Cottonwood Creek, Tributary of the Snake River

LOCATION:

Legal description and tie:

(Point of Diversion)

Headgate Location: S 67° 40' W, 3270 feet from North quarter corner
of Section 13, Township 44 North, Range 116 West.

WATER RIGHT:

Appropriator: Jackson Hole Preserve, Inc.

Certificate Record Number: 61-274

Permit Number: 19705

Date of priority: October 29, 1941

Quantity of Water: 0.056 c.f.s.

Purpose: Domestic

Irrigate Land Description:

(T 44 N, R 116 W)

This appropriation is limited to domestic use in the NW $\frac{1}{4}$ NW $\frac{1}{4}$,
Section 13, Township 44 North, Range 116 West, in an amount not to
exceed 0.056 cubic foot per second.

SUMMARY OF STATUS:

The above land was conveyed to the United States of America by the
Jackson Hole Preserve, Incorporated, as contained in National Park Service
Deed Number 2.

The Water Right is presently used for a domestic water supply for the
Jenny Lake Lodge.

IN TESTIMONY WHEREOF, I, L. G. BISHOP, President of the State Board of Control, have hereunto set my hand
this 26th day of March, A. D. 19 48, and caused the seal of said Board to be hereunto affixed.
Attest: [Signature] Ex-officio Secretary. [Signature] President.

Form 10-174
(Rev. 8-56)UNITED STATES DEPARTMENT OF THE INTERIOR
NATIONAL PARK SERVICE

COMPLETION REPORT OF CONSTRUCTION PROJECT

REGION Two	AREA Grand Teton National Park	COUNTY Teton	STATE Wyoming
PROJECT OR JOB TITLE Water and Sewer Systems			PCP NO. U58 U59
LOCATION IN AREA Jenny Lake Lodge		MASTER PLAN NO. NP-GT 3200	BUILDING NO.
WORKING DRAWING NO. AND TITLE NP-GT 3210 Water & Sewer Systems			WORK ORDER NO. 332.14 332.17
APPROPRIATION TITLE AND SYMBOL 14X1035			
CONTRACT NO. 14-10-216-252		DATE WORK STARTED Setp. 3, 1957	DATE WORK COMPLETED June 25, 1958
NAME OF CONTRACTOR Landon Construction Company		ADDRESS 814 South Durbin Street Casper, Wyoming	

COST ANALYSIS

CONSTRUCTION ITEMS	QTY.	UNIT COST IN PLACE	TOTAL COST IN PLACE
See Attached Bid Schedule			127,311.53
Unsuccessful attempt to drill water well 332.14 Cope Drilling Company - 14-10-216-239 Day Labor Costs			882.00 30.76
Facilitating Services Cost Breakdown: 332.14 - \$83,268.31 332.17 - \$43,750.98			795.00
Fiscal Clearance: <i>Harold P. Danz</i> Harold P. Danz, Supervisory Accountant			
TOTAL			129,019.29

SUMMARY OF EXPENDITURES

PERSONAL SERVICES	EQUIPMENT	MATERIALS AND SUPPLIES 30.76
OTHER Cope Drilling Company - \$882.00; Facilitating Services \$795.00; Total \$1,677.00		

CHANGE ORDERS

ORIGINAL CONTRACT AMOUNT \$116,045.00	FIRST \$10,870.00	SECOND	THIRD
FINAL CONTRACT AMOUNT \$127,311.53	FOURTH	FIFTH	SIXTH

THIS PROJECT OR JOB HAS BEEN COMPLETED IN ACCORDANCE WITH
APPROVED DRAWINGS, SPECIFICATIONS, AUTHORIZED CHANGES

SUBMITTED BY (Name and title) <i>D. L. Bressler</i> Project Supervisor	DATE November 3, 1958
APPROVED BY (Name and title) <i>E. R. Oberhansley</i> Superintendent	DATE

(ATTACH NARRATIVE STATEMENT, PHOTOGRAPHS, AND "AS BUILT" DRAWINGS TO THIS FORM)

Brief History

The contract for construction of the Jenny Lake Lodge Sewer and Water Systems was awarded to Landon Construction Company of Casper, Wyoming. Construction work started on September 3, 1957. Work was completed except for the pump installation and minor adjustments by November 9, 1958. A stop order was issued due to adverse weather conditions on November 9, 1957.


A start order was issued June 2, 1958 at which time the contractor installed pumps and completed the project except for testing of electric components of system.


Since electricity was not available, an extension of time was granted and the work was completed on June 25, 1958.

Difficulties Encountered

It was intended that the source of water be obtained from a deep well located at the reservoir site. The deep well was not successful and as a result change order #1 was issued to Landon Construction Company to construct a shallow well near the creek west of the lodge. A chlorinator was installed at the shallow well to conform to Public Health Service requirements.

Maps and Miscellaneous Information

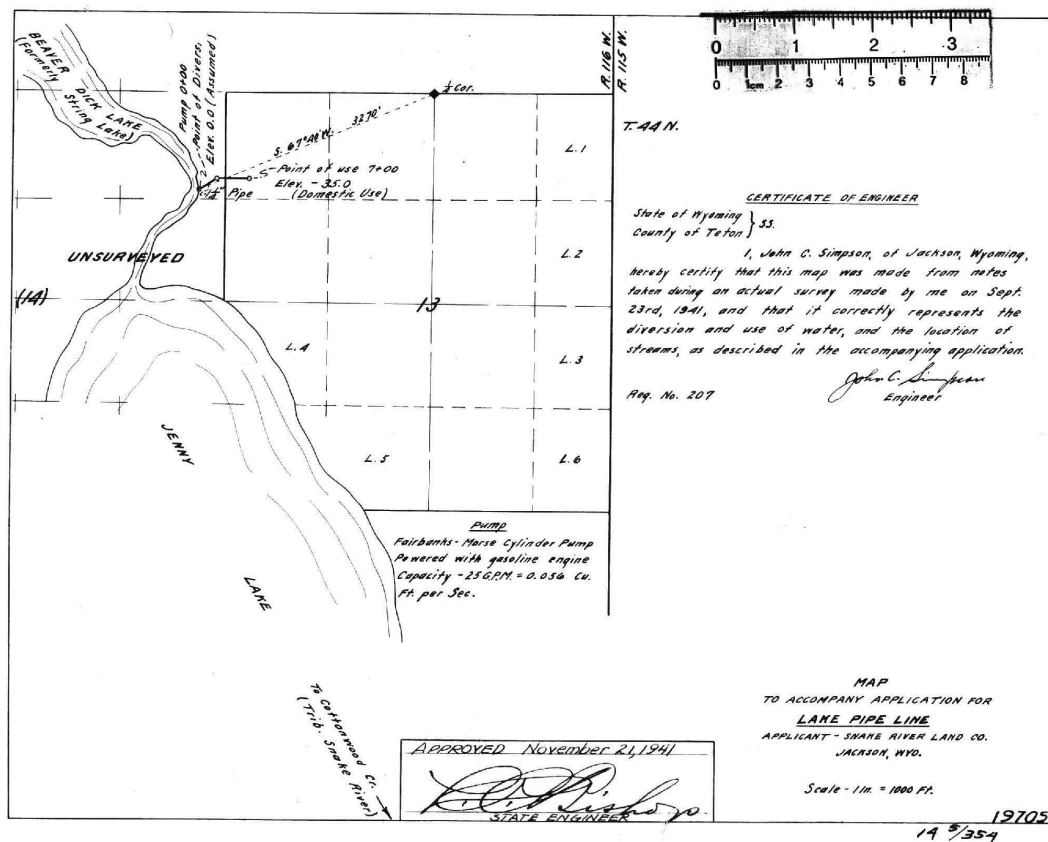

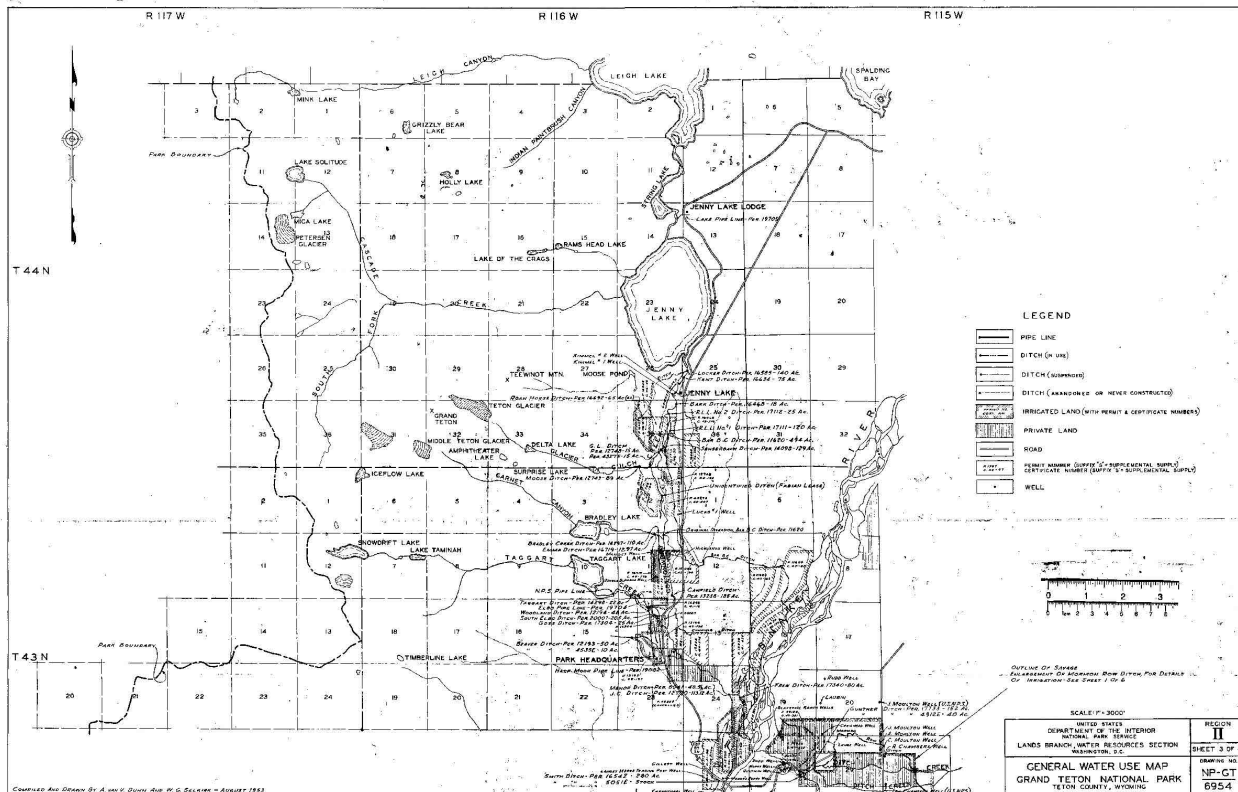

Docket Information

Number of Documents in Docket 6

Documents Dated from 10/29/1941 to 8/15/1953

Docket Compiled: 3/30/2011
